BACKWASHING FILTER STARTUP PROCEDURE

V. 10/22/2026


STEP 1

Before Startup

1.) Verify incoming water pressure does not exceed 80 psi.
2.) Verify the inlet and outlet connections are correct and secure.
3.) Verify the drain line is connected, secured, unobstructed, and terminates with an approved air gap.
4.) Confirm the system is in Bypass.
5.) Verify electrical power is available.

→ **IMPORTANT:** Inspect plumbing and drain connections for leaks throughout startup.

Figure 2
BYPASS OPERATION

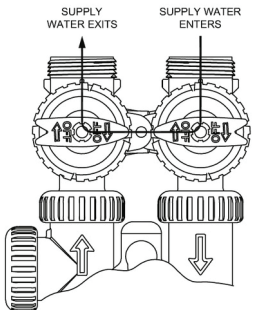

BYPASS OPERATION
both handles positioned toward the center of the bypass

STEP 2

Restore Water & Flush

1.) Open a downstream cold-water faucet.
2.) Slowly open the building's main water supply.
3.) Flush until the water runs clear and all air is expelled.
4.) Close the faucet.

STEP 3

Power & Verify Valve

1.) Plug the system into an electrical outlet.
2.) Pull the battery tab located behind the faceplate.
3.) Verify the valve is properly programmed for the installed filter.
4.) Verify the regeneration schedule is set for every 7 days.
5.) Verify the correct time of day.

⚠

CAUTION: Do not remove the battery tab before plugging the valve into an electrical outlet. Valve programming may be damaged if the battery tab is removed before the valve is plugged into an electrical outlet.

STEP 4

Initiate Backwash


1.) Press and hold REGEN to initiate a manual regeneration.
2.) Allow the valve motor to stop in Backwash.
3.) Unplug the valve to hold it in Backwash.

STEP 5

Fill & Purge Mineral Tank

1.) Crack the inlet side of the bypass valve approximately 1/8 turn.
2.) Allow the mineral tank to fill slowly. Introducing water slowly helps prevent media loss to drain.
3.) As the air clears, gradually open the inlet farther.
4.) Continue until the inlet is fully open and full backwash flow is established.
5.) Verify steady flow to drain.
6.) Continue backwashing until the discharge is clear and free of air.
7.) Inspect the system and drain connections for leaks.

Figure 3

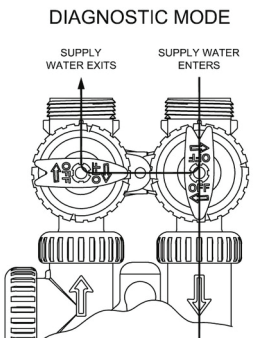

DIAGNOSTIC MODE
inlet open and outlet closed. Begin initial filling with the inlet only partially open, then gradually open fully.

STEP 6

Complete Rinse


1.) Plug the control valve back into power.
2.) Press REGEN to advance the valve to Rinse.
3.) Allow the programmed Rinse cycle to complete.

STEP 7

Place Filter in Normal Operation

1.) Allow the valve to return to Normal Operation.
2.) Open the outlet side of the bypass valve.
3.) Open a downstream cold-water faucet and flush until the water runs clear.
4.) Inspect the complete installation for leaks.

Figure 1

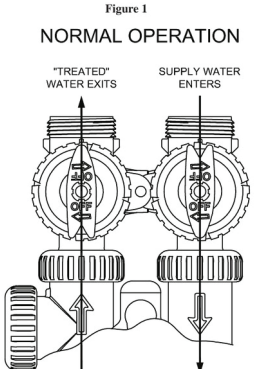

NORMAL OPERATION
inlet and outlet handles positioned in the direction of flow.

STEP 8

Final Verification

1.) Verify the control valve is in Normal Operation and displays the correct time of day.
2.) Verify the next automatic regeneration is scheduled according to the 7-day setting.
3.) Operate plumbing fixtures to verify proper water flow and system operation.
4.) Test water to verify contaminant reduction.
4.) Confirm the installation area is clean and ready for normal operation.
5.) Review basic operation and maintenance with the customer, answer questions, and turn the system over to the customer.

TECHNICAL BASIS

BritaPRO 7-day Backwash -> Rinse specification; Clack WS1 non-regenerating filter sequence and Clack system-startup guidance.
